Go-live: how does it go live?

Agent 06 · CI/CD pipeline

Module	Subscription Management
Owner	CI/CD pipeline
Version	1.0, for review
Date	12 October 2026

Document control

Document	Subscription Management - Agent 06 - Go-live
Subject	Agent 06 · CI/CD pipeline
Version	1.0
Date	2026-10-12
Status	For review
Owner	CI/CD pipeline
Generated by	`src/generators/emit-client-pack.js`
Source	`docs/client-pack/06-go-live.md`
Source blueprint	`49f2c22e6c8f`
Prepared by	Ascendion
Classification	Ascendion Confidential

Contents

1. Purpose and scope

2. The agents in this phase

    2.1 CI/CD pipeline

3. Inputs

4. Outputs and results

5. Release pipeline

6. Cutover steps

7. Cutover checklist

8. Review gate and items to confirm

9. Where the artifacts live

Figures

Figure 1. Every change passes every check before it reaches Azure

1. Purpose and scope

We release the module to the cloud through CI/CD, one business domain at a time, with a way back at every step. The target deployment on Azure, its environments and its recovery targets are in the HLD, section 7.

2. The agents in this phase

2.1 CI/CD pipeline

> **What it does**
>
> Re-runs every check on each change and releases to the target cloud (Azure in the demo), one business domain at a time.
>
> **What it produces**
>
> - Tested release
> - Health check after deploy

3. Inputs

- An approved change, with every check passing
- The infrastructure definition (Bicep) for the target

4. Outputs and results

- A tested release on Azure
- A health check after every deploy

5. Release pipeline

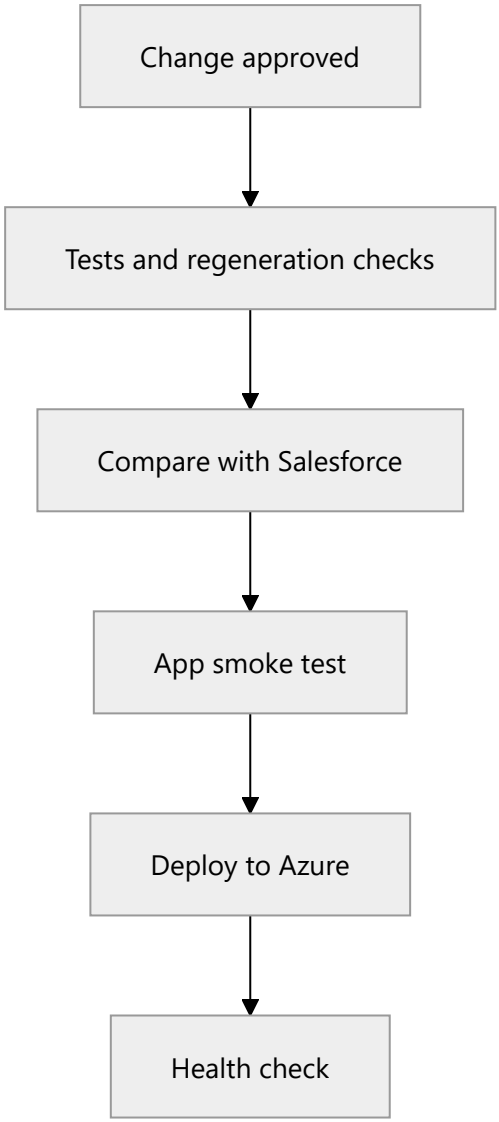


Figure 1. *Every change passes every check before it reaches Azure*

6. Cutover steps

Each domain goes through these steps in its wave; the waves and which system masters each domain are in the HLD, section 8.3.

Step	What happens
1 Shadow	Both systems run; we turn differences into new tests
2 Reporting first	Reports move first, so the numbers are trusted
3 Module switch	Writes move in a short freeze; Salesforce stays read-only
4 Integrations	Other systems move one by one
5 Decommission	Licences reduce at renewal

7. Cutover checklist

We sign this off at go-live, for each domain.

Item	Done when	Prepared in
Integration credentials	Every new credential is live and tested	Agent 03 - Build, section 5
Scheduled jobs	Off in Salesforce and on in Azure, in one step	Agent 04 - Migrate, section 7
Open approvals and paused flows	Finished or carried over	Agent 04 - Migrate, section 7
History	Archive loaded	Agent 04 - Migrate, section 6
Salesforce	Kept read-only until the domain has moved	This document, section 6

8. Review gate and items to confirm

What a person checks before the next phase starts

- Every check passes on the release candidate
- The rollback has been rehearsed

What we ask you to confirm

- The cutover date and freeze window for each domain
- Who signs off the cutover checklist
- The licence renewal date

9. Where the artifacts live

Artifact	Location
Infrastructure and deploy scripts	`adlc/6-go-live/infra/`
Pipeline definition	`.github/workflows/crm-genie.yml`
