Moving Subscription Management off Salesforce

Overview of the six phases

Module	Subscription Management
Owner	All agents
Version	1.0, for review
Date	7 October 2026

Ascendion Confidential

Document control

Document	Subscription Management - 00 - Overview
Subject	Overview of the six phases
Version	1.0
Date	2026-10-07
Status	For review
Owner	All agents
Generated by	`src/generators/emit-client-pack.js`
Source	`docs/client-pack/00-overview.md`
Source blueprint	`fc71a1458dce`
Prepared by	Ascendion
Classification	Ascendion Confidential

Contents

1. Purpose and scope
2. Six phases, one or more agents each
3. Where we are today
4. The documents in this pack
5. How we work

Figures

Figure 1. The agentic workflow: one or more agents per phase, with a repair loop when a check fails

1. Purpose and scope

This pack describes how we move the **Subscription Management** module from Salesforce to a client-owned platform on Azure. Subscription Management is a custom module built in the org (the Subscription and Subscription Line objects); it is not a Salesforce product. It is the first domain of a platform designed to take every module of the org, one wave at a time (HLD, sections 5 and 8.3).

- We move the module, its records, rules, calculations and permissions
- We keep every one of them working exactly as it does today
- We prove it with numbers before anyone switches over; Salesforce stays live until then

2. Six phases, one or more agents each

Each phase answers one question. Each phase is reviewed before the next begins.

Phase	Question	Agents	Answer
1 Discover	What is in the org?	Extraction	Objects, fields, rules, flows, Apex, security and data
2 Design	What does it mean?	Modelling	One platform-independent model of the org
3 Build	What replaces it?	Schema, Logic, Security	Database, business rules, security and services, generated from the model
4 Migrate	How does the data move?	Data load	In dependency order, with Salesforce record IDs kept
5 Validate	Does it behave the same?	Verification, Repair	Calculated values and rule outcomes checked against the org
6 Go-live	How does it go live?	CI/CD pipeline	Released to the cloud through CI/CD, one domain at a time

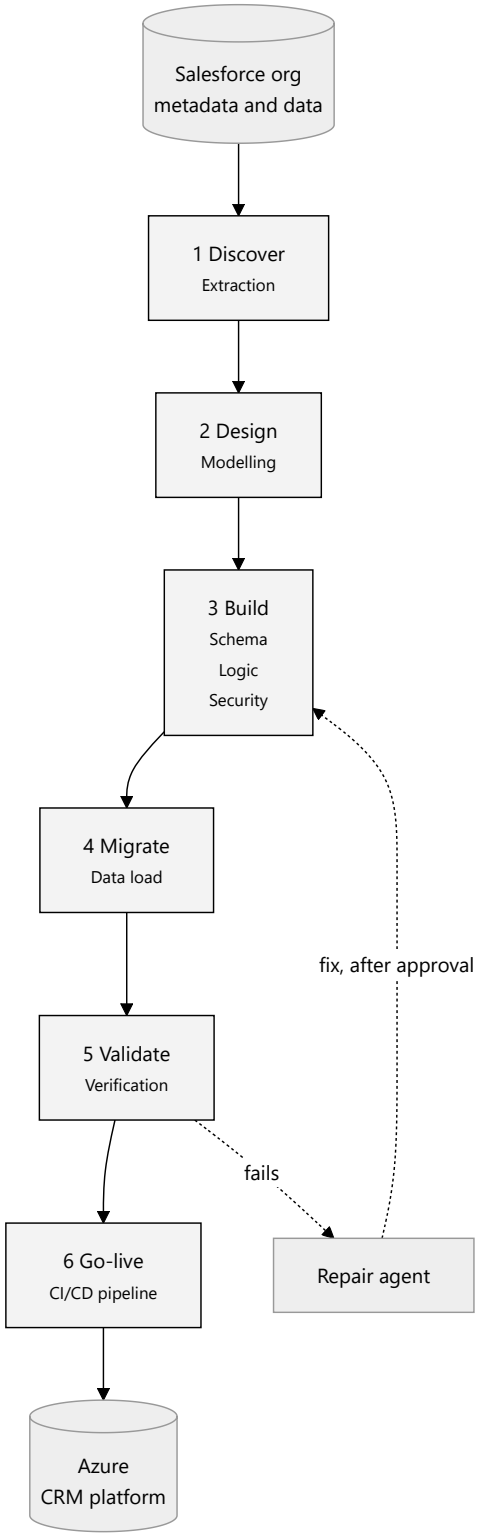


Figure 1. *The agentic workflow: one or more agents per phase, with a repair loop when a check fails*

3. Where we are today

Phase	Status	Results in
1 Discover	Complete	Agent 01 - Discover, section 4

Phase	Status	Results in
2 Design	Complete	Agent 02 - Design, section 4
3 Build	Database, rules and access built; custom code translation in progress	Agent 03 - Build, section 4
4 Migrate	All module records loaded and reconciled	Agent 04 - Migrate, section 4
5 Validate	All calculated values match; two tests wait for custom code	Agent 05 - Validate, section 4
6 Go-live	Proof of concept running on Azure; cutover planned	Agent 06 - Go-live

4. The documents in this pack

Document	What it covers
Agent 01 - Discover	What we found in the org, and what Salesforce keeps
Agent 02 - Design	The model, vendor packages, and a guide to the design documents
Agent 02 - High-Level Design	arc42 architecture with C4 views, business processes and decisions
Agent 02 - Low-Level Design	Tables, rules, automations, security, load order and traceability
Agent 03 - Build	What we built, and the integration credentials to renew
Agent 04 - Migrate	Records moved, history archive and work in progress
Agent 05 - Validate	Parity results and built-in platform behaviour
Agent 06 - Go-live	Release pipeline and cutover
KB 01 - Best Practices	Engineering best practices we follow, with references
KB 02 - Architecture	Architecture best practices, patterns and standards, with references

5. How we work

Principle	What it means
Modular	We can run, re-run or replace any agent. A shared model decouples Salesforce from the target.
Scalable	We split large orgs into business domains. Domains migrate in parallel.
Controlled	We sign off every phase, fully audited. Automated checks run before every release.
